

VISION Resistivity
Dual Frequency
Recorded Mode, Run 9

Schlumberger

Country: Norway

Company: Equinor

Well: 31/5-7

Field: Eos

Rig Name: West Hercules

Country: Norway

Latitude: 60° 34' 35.14" N

UWID:

Longitude: 3° 26' 36.13" E

Rig Name:

West Hercules

Block: 31/5

Rig Type:

Semi-Submersible

FL: Norwegian North Sea

FL1: Section: 8 1/2 in.

FL2: Job no.: 19SCA0085

Log Measured From: - Drill Floor: 31.00 m
Permanent Datum: - Mean Sea Level

Ground Level: 307.00 m

Acquisition Dates: 29-Dec-2019 -- 30-Dec-2019

Other Services:

Log Interval: 2544.00(m) -- 2593.00(m)

Direction & Inclination (Surveys)

Index Types: Measured Depth

Annular Pressure While Drilling

Index Scales: 1:500

geoVISION Bit Resistivity

Depth Source: Driller's Depth

Depth Sensor: 3rd Party Depth

Print Type: Final

Spud Date: 02-Dec-2019


Disclaimer


THE USE OF AND RELIANCE UPON THIS RECORDED-DATA BY THE HEREIN NAMED COMPANY (AND ANY OF ITS AFFILIATES, PARTNERS, REPRESENTATIVES, AGENTS, CONSULTANTS AND EMPLOYEES) IS SUBJECT TO THE TERMS AND CONDITIONS AGREED UPON BETWEEN SCHLUMBERGER AND THE COMPANY, INCLUDING: (a) RESTRICTIONS ON USE OF THE RECORDED-DATA; (b) DISCLAIMERS AND WAIVERS OF WARRANTIES AND REPRESENTATIONS REGARDING COMPANY'S USE AND RELIANCE UPON THE RECORDED-DATA; AND (c) CUSTOMER'S FULL AND SOLE RESPONSIBILITY FOR ANY INFERENCE DRAWN OR DECISION MADE IN CONNECTION WITH THE USE OF THIS RECORDED-DATA.

Contents

1. Header
2. Disclaimer
3. Contents
4. Well Sketch
5. Borehole Size/Casing/Tubing Record
6. Operational Run Summary
7. Borehole Fluids
8. Remarks and Equipment Summary
9. Run 9 VISION Resistivity - Dual Frequency
 - 9.1 Integration Summary
 - 9.2 Software Version
 - 9.3 Composite Summary
 - 9.4 Log (Resistivity - Dual Frequency)
 - 9.5 Parameter Listing
10. Calibration Report
11. Tail

Well Sketch

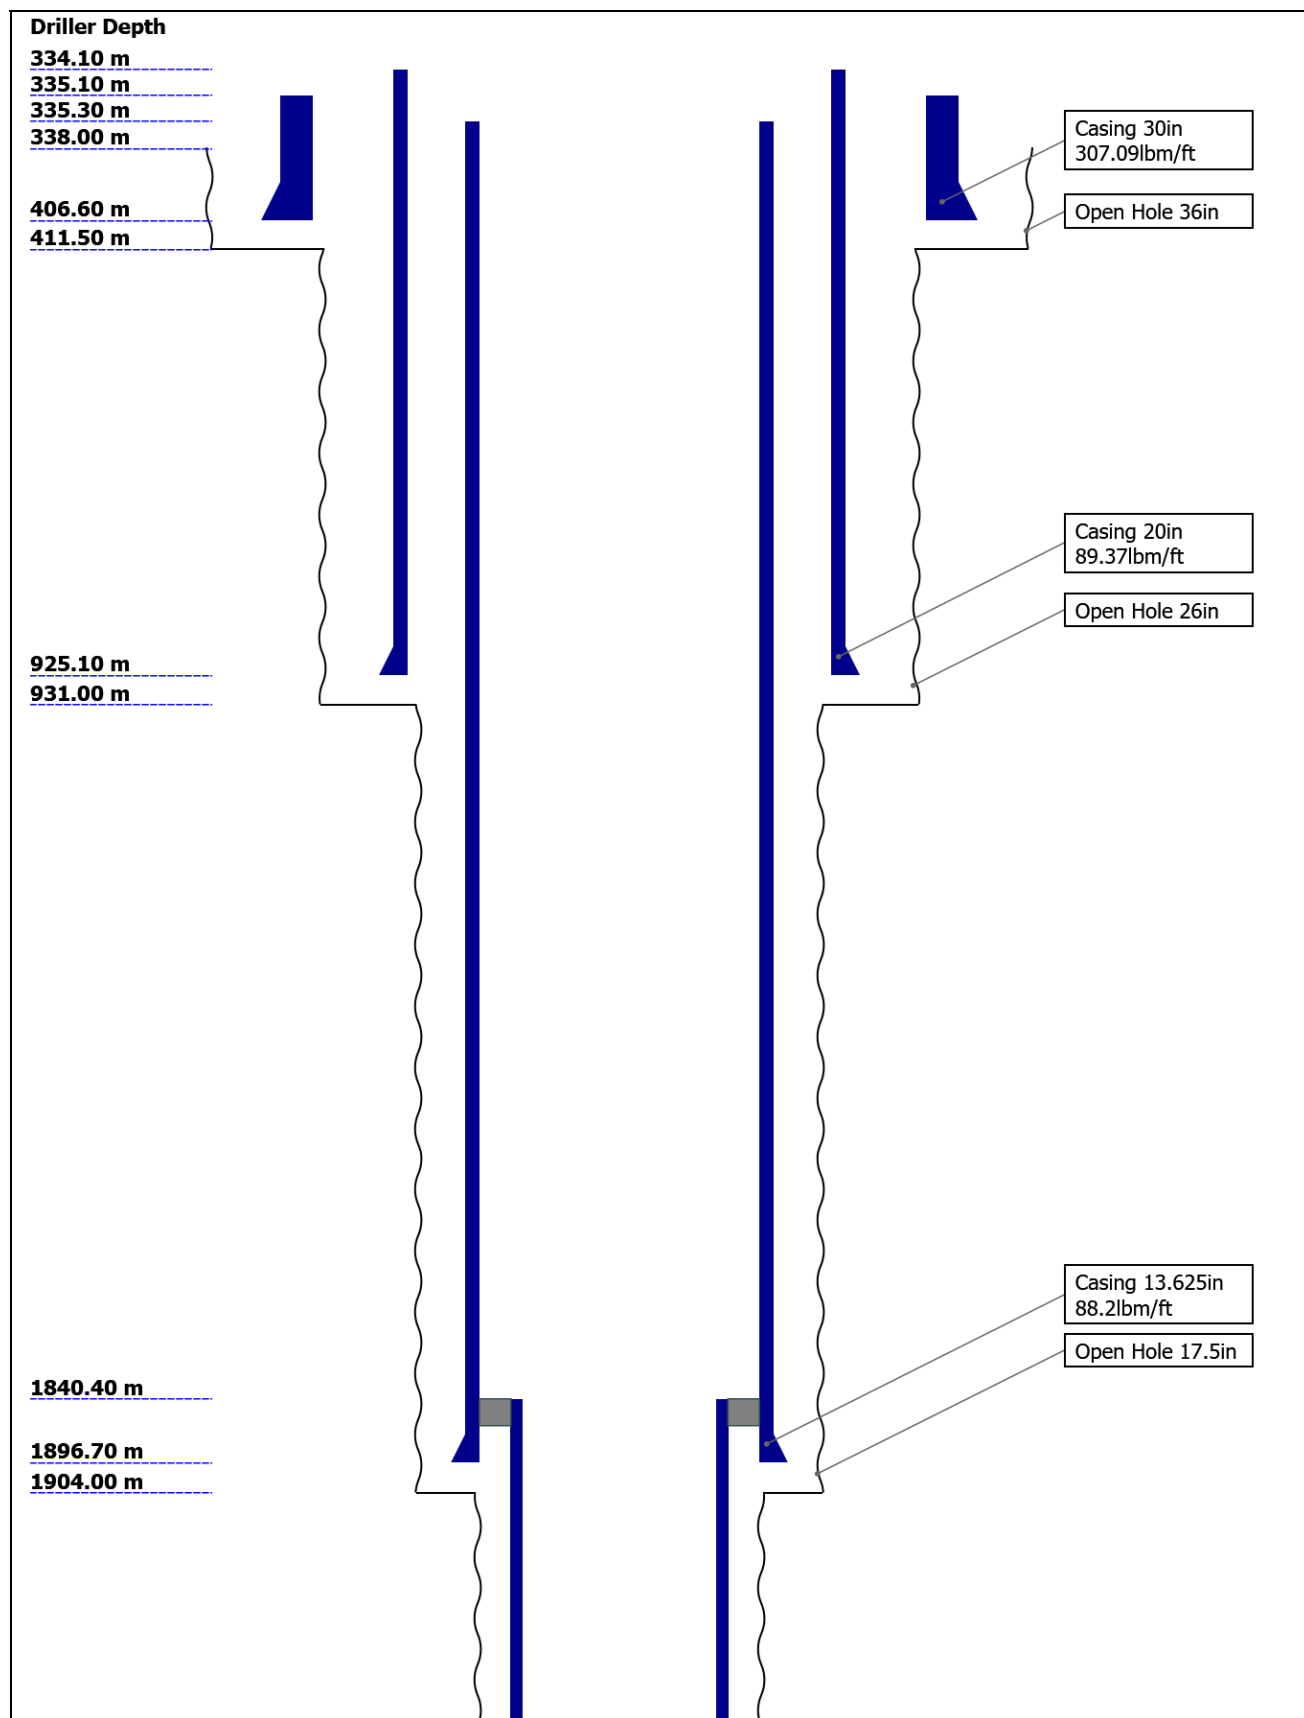

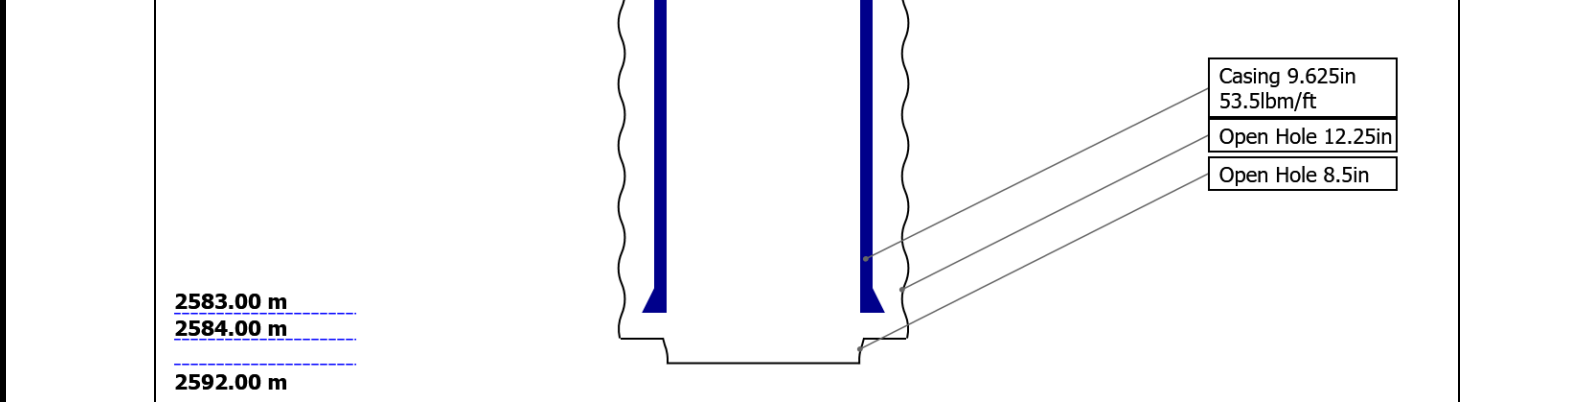

Borehole Size/Casing Record

Bit						
Bit Size (in)	36	26	17.5	12.25	8.5	
Top Driller (m)	338	411.5	931	1904	2584	
Bottom Driller (m)	411.5	931	1904	2584	2592	
Casing						
Size (in)	30	20	13.625	9.625		
Weight (lbm/ft)	307.09	89.37	88.2	53.5		
Inner Diameter (in)	27.067	18.73	12.375	8.535		
Grade	X56	N80	P110	P110		
Top Driller (m)	335.1	334.1	335.3	1840.4		
Bottom Driller (m)	406.6	925.1	1896.7	2583		


Operational Run Summary

Parameter (unit)	Run 9					
Date Log Started	29-Dec-2019					
Time Log Started	06:12:03					
Date Log Finished	30-Dec-2019					
Time Log Finished	05:04:18					
Bit Size (in)	8.500					
Bit Start Depth (m)	2584.00					
Bit Stop Depth (m)	2592.00					
Top Log Interval (m)	2584.70					
Bottom Log Interval (m)	2591.22					
Max Hole Deviation (deg)	1.10					
Azimuth of Max Deviation (deg)	133.27					
Logging Unit Number	A615					
Logging Unit Location	Service Office					
Recorded By	S.Kroevel					
Witnessed By	J.Eikenes					
Service Order Number	19SCA0085					

Borehole Fluids

Remarks and Equipment Summary

ARC6-H0143-1 9 88 arcVISION

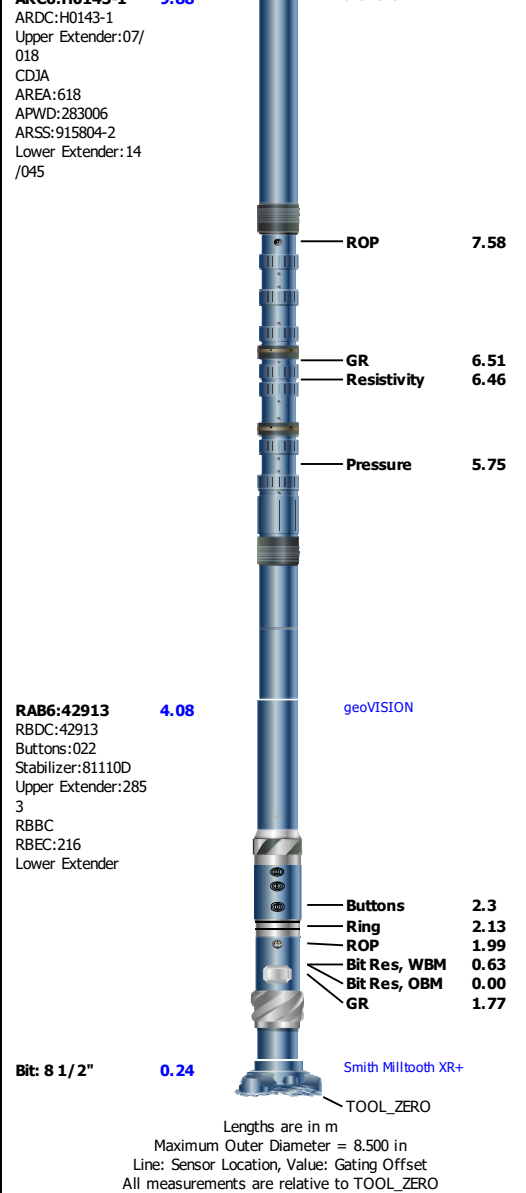

Run 9

VISION Resistivity - Dual Frequency

Software Version

Acquisition System		Version	
Maxwell 2019.2		9.2.113335.3100	
Application Patch		DnM_TestKit-XceedCPU41-2019.2_9.2.114181	
Computation	Description	Version	
ARCResistivity	ARC Resistivity Computation Package for ARC Tool Family	9.2.113335.3100	
ARC6GammaRay	ARC6 Gamma Ray Computation Package for both Real-time and Recorded Mode	9.2.113335.3100	
GVRRes	GVR Resistivity Computation Package for both Real-time and Recorded Mode	9.2.113335.3100	
Tool Interface	System Version	Loaded Version	
HSPM	2019.0c.001	9.2.113335.3100	
Tool Elements	Description	Software Version	Firmware Version
RBEC	Electronics Chassis Assembly for RAB6-C	9.2.113335.3100	V8.8B
DRILLING_SURFACE	DRILLING_SURFACE	9.2.113335.3100	
ARDC	ARC 6.75 Inch Tool Drill Collar	9.2.113335.3100	V9.7B

Pass Summary

Run Name	Pass Objective	Direction	Top	Bottom	Start	Stop	Include Parallel Data
Run 9	Drilling	Down	720.04 m	2591.89 m	29-Dec-2019 6:12:03 AM	30-Dec-2019 5:04:18 AM	Yes

Resistivity Time After Bit (ARTM) ARC6 0h10 Rate of penetration averaged over the last 5 ft (1.5 m) (ROP5) RT 200m/h0 Gamma Ray (GR_ARC) ARC6 RM 0gAPI150	Phase Shift Resistivity 40 inch Spacing at 2 MHz, Environmentally Corrected. (P40H) ARC6 RM		Attenuation Resistivity 40 inch Spacing at 2 MHz, Environmentally Corrected. (A40H) ARC6 RM		Attenuation Resistivity 40 inch Spacing at 400 KHz, Environmentally Corrected (A40L) ARC6 RM	
	0.2ohm.m200		0.2ohm.m200		0.2ohm.m200	
	Phase Shift Resistivity 34 inch Spacing at 2 MHz, Environmentally Corrected. (P34H) ARC6 RM		Attenuation Resistivity 34 inch Spacing at 2 MHz, Environmentally Corrected (A34H) ARC6 RM		Phase Shift Resistivity 40 inch Spacing at 400 KHz, Environmentally Corrected. (P40L) ARC6 RM	
	0.2ohm.m200		0.2ohm.m200		0.2ohm.m200	
	Phase Shift Resistivity 28 inch Spacing at 2 MHz, Environmentally Corrected. (P28H) ARC6 RM		Attenuation Resistivity 28 inch Spacing at 2 MHz, Environmentally Corrected (A28H) ARC6 RM		Phase Shift Resistivity 34 inch Spacing at 400 KHz, Environmentally Corrected. (P34L) ARC6 RM	
	0.2ohm.m200		0.2ohm.m200		0.2ohm.m200	
	Phase Shift Resistivity 22 inch Spacing at 2 MHz, Environmentally Corrected. (P22H) ARC6 RM		Attenuation Resistivity 22 inch Spacing at 2 MHz, Environmentally Corrected (A22H) ARC6 RM		Phase Shift Resistivity 28 inch Spacing at 400 KHz, Environmentally Corrected. (P28L) ARC6 RM	
	0.2ohm.m200		0.2ohm.m200		0.2ohm.m200	
	Phase Shift Resistivity 16 inch Spacing at 2 MHz, Environmentally Corrected. (P16H) ARC6 RM		Attenuation Resistivity 16 inch Spacing at 2 MHz, Environmentally Corrected (A16H) ARC6 RM		Phase Shift Resistivity 22 inch Spacing at 400 KHz, Environmentally Corrected. (P22L) ARC6 RM	
	0.2ohm.m200		0.2ohm.m200		0.2ohm.m200	
	Bit Resistivity (RES_BIT) RAB6 RM				Phase Shift Resistivity 16 inch Spacing at 400 KHz, Environmentally Corrected. (P16L) ARC6 RM	
	0.2ohm.m200				0.2ohm.m200	
Description: Format: Log (Resistivity - Dual Frequency) Index Scale: 1:500 Index Unit: m Index Type: Measured Depth Creation Date: 20-Jan-2020 10:54:55						

Channel Processing Parameters

Run 9: Parameters

Parameter	Description	Tool	Value	Unit
ABNT	Abnormal Transmitter Indicator	ARC6	NO_TX_FAILED	
BH_COMPUTE	Borehole Effect Computation Option	ARC6	No	
BHK	Drilling Fluid Potassium Concentration	Borehole	6.7	%
BHT	Bottom Hole Temperature	Borehole	38	degC
BS	Bit Size	DNMSESSION	Depth Zoned	in
DEPTH_SEL	Depth Selection Parameter	DNMSESSION	Driller's Depth	
DFD	Drilling Fluid Density	Borehole	1.15	g/cm3
DFT_CATEGORY	Drilling Fluid Type	Borehole	Water	
ERRCT	Percentage Error Cutoff	ARC6	4.5	%
GRSE_RM	Generalized Mud Resistivity Selection for Recorded Mode	Borehole	REMS(RM)	
GRSH	Gamma Ray Shale	ARC6	1000	gAPI
GTSE_RM	Generalized Temperature Selection for Recorded Mode	Borehole	DHAT(RM)	
HIGH_BLEND	High Resistivity Threshold for Blending	ARC6	2	ohm.m
INVAS_COMPUTE	Invasion Computation Option	ARC6	No	
LOW_BLEND	Low Resistivity Threshold for Blending	ARC6	1	ohm.m
MST	Mud Sample Temperature	Borehole	18	degC
MSWS	ARCWizard Model Switch Window Size	ARC6	152.4	cm
MULTIEFFECT_COMPUTE	Multi-effect Computation Option	ARC6	No	

PRTD	ARCWizard Preferred Resistivity Log for Rt Display while Multi-Effects	ARC6	P34B	
RMS	Resistivity of Mud Sample	Borehole	0.07	ohm.m
T1WM	ARCWizard Weight Multiplier to Measurements for Transmitter 1	ARC6	1	
T2WM	ARCWizard Weight Multiplier to Measurements for Transmitter 2	ARC6	1	
T3WM	ARCWizard Weight Multiplier to Measurements for Transmitter 3	ARC6	1	
T4WM	ARCWizard Weight Multiplier to Measurements for Transmitter 4	ARC6	1	
T5WM	ARCWizard Weight Multiplier to Measurements for Transmitter 5	ARC6	1	
ATMP_ARC	ARC Temperature Selection	ARC6	Annular	
TEMP_SEL_RAB	RAB Temperature Selection	RAB6	Tool	
UNIFORM_COMPUTE	Uniform Rock Computation Option	ARC6	No	

Depth Zone Parameters

Parameter	Value	Start (m)	Stop (m)
BS	12.25	2544	2584
BS	8.5	2584	2592

All depth are actual.

Tool Control Parameters

Run 9: Parameters

Parameter	Description	Tool	Value	Unit
OFFBTM_TH	Threshold for deciding whether the bit is off bottom	DNMSESSION	0	m

Calibration Report

RAB6 (GeoVision Resistivity 675) Calibration - Run 9

Primary Equipment :

Electronics Chassis

RBEC

216

M21V - Resistivity

Master (Time Frame File): 16:32:26 08-Aug-2019

Measurement	Unit	Phase	Nominal	Low Limit	Actual	High Limit	
Monitor 2 at T1 Calibration Coefficient		Master	1.0000	0.9750	1.0000	1.0250	

M22V - Resistivity

Master (Time Frame File): 16:32:26 08-Aug-2019

Measurement	Unit	Phase	Nominal	Low Limit	Actual	High Limit	
Monitor 2 at T2 Calibration Coefficient		Master	1.0000	0.9750	1.0020	1.0250	

M01V - Resistivity

Master (Time Frame File): 16:32:26 08-Aug-2019

Measurement	Unit	Phase	Nominal	Low Limit	Actual	High Limit	
Monitor 0 at T1 Calibration Coefficient		Master	1.0000	0.9750	0.9950	1.0250	

M02V - Resistivity

Master (Time Frame File): 16:32:26 08-Aug-2019

Measurement	Unit	Phase	Nominal	Low Limit	Actual	High Limit	
Monitor 0 at T2 Calibration Coefficient		Master	1.0000	0.9750	0.9980	1.0250	

R1V - Resistivity

Master (Time Frame File): 16:32:26 08-Aug-2019

Measurement	Unit	Phase	Nominal	Low Limit	Actual	High Limit	
Ring at T1 Calibration Coefficient		Master	1.0000	0.9750	1.0000	1.0250	

R2V - Resistivity

Master (Time Frame File): 16:32:26 08-Aug-2019

Measurement	Unit	Phase	Nominal	Low Limit	Actual	High Limit	
Ring at T2 Calibration Coefficient		Master	1.0000	0.9750	1.0030	1.0250	

BDM1 - Resistivity

Master (Time Frame File): 16:32:26 08-Aug-2019

Measurement	Unit	Phase	Nominal	Low Limit	Actual	High Limit	
Button Deep at T1 Calibration Coefficient		Master	1.0000	0.9750	1.0070	1.0250	

BDM2 - Resistivity

Master (Time Frame File): 16:32:26 08-Aug-2019

Measurement	Unit	Phase	Nominal	Low Limit	Actual	High Limit	
Button Deep at T2 Calibration Coefficient		Master	1.0000	0.9750	1.0100	1.0250	

BMM1 - Resistivity

Master (Time Frame File): 16:32:26 08-Aug-2019

Measurement	Unit	Phase	Nominal	Low Limit	Actual	High Limit	
Button Medium at T1 Calibration Coefficient		Master	1.0000	0.9750	0.9990	1.0250	

BMM2 - Resistivity

Master (Time Frame File): 16:32:26 08-Aug-2019

Measurement	Unit	Phase	Nominal	Low Limit	Actual	High Limit	
Button Medium at T2 Calibration Coefficient		Master	1.0000	0.9750	1.0020	1.0250	

BSM1 - Resistivity

Master (Time Frame File): 16:32:26 08-Aug-2019

Measurement	Unit	Phase	Nominal	Low Limit	Actual	High Limit	
Button Shallow at T1 Calibration Coefficient		Master	1.0000	0.9750	1.0000	1.0250	

BSM2 - Resistivity

Master (Time Frame File): 16:32:26 08-Aug-2019

Measurement	Unit	Phase	Nominal	Low Limit	Actual	High Limit	
Button Shallow at T2 Calibration Coefficient		Master	1.0000	0.9750	1.0030	1.0250	

PGR - Gamma Ray: Blanket

Master (Time Frame File): 14:06:21 18-Dec-2019

Measurement	Unit	Phase	Nominal	Low Limit	Actual	High Limit	
Gamma Ray Calibration Gain		Master	1.0000	0.7500	0.9838	1.2500	

ARC6 (Array Resistivity Compensated 675) Calibration - Run 9

Primary Equipment :

Elec. Chassis HP w/o AIM Receiver

AREA

618

RESAIRCAL - Resistivity: Air

Master (Time Frame File): 15:26:50 07-Dec-2019

Measurement	Unit	Phase	Nominal	Low Limit	Actual	High Limit	
Attenuation T1 at 2 MHz	dB	Master	8.500	6.500	7.951	10.500	
Attenuation T2 at 2 MHz	dB	Master	6.500	4.500	6.997	8.500	
Attenuation T3 at 2 MHz	dB	Master	4.500	2.500	4.584	6.500	
Attenuation T4 at 2 MHz	dB	Master	4.600	2.600	4.904	6.600	
Attenuation T5 at 2 MHz	dB	Master	3.600	1.600	3.142	5.600	
Phase Shift T1 at 2 MHz	deg	Master	0.100	-3.900	1.927	4.100	
Phase Shift T2 at 2 MHz	deg	Master	0.100	-3.900	-1.871	4.100	
Phase Shift T3 at 2 MHz	deg	Master	0.100	-3.900	1.878	4.100	
Phase Shift T4 at 2 MHz	deg	Master	0.100	-3.900	-1.879	4.100	
Phase Shift T5 at 2 MHz	deg	Master	0.100	-3.900	1.856	4.100	
Attenuation T1 at 400 KHz	dB	Master	8.500	6.500	7.970	10.500	
Attenuation T2 at 400 KHz	dB	Master	6.500	4.500	6.989	8.500	
Attenuation T3 at 400 KHz	dB	Master	4.500	2.500	4.593	6.500	
Attenuation T4 at 400 KHz	dB	Master	4.600	2.600	4.889	6.600	
Attenuation T5 at 400 KHz	dB	Master	3.600	1.600	3.160	5.600	
Phase Shift T1 at 400 KHz	deg	Master	0.100	-3.900	-0.666	4.100	
Phase Shift T2 at 400 KHz	deg	Master	0.100	-3.900	0.584	4.100	
Phase Shift T3 at 400 KHz	deg	Master	0.100	-3.900	-0.629	4.100	
Phase Shift T4 at 400 KHz	deg	Master	0.100	-3.900	0.582	4.100	
Phase Shift T5 at 400 KHz	deg	Master	0.100	-3.900	-0.643	4.100	

GRGAIN - Gamma Ray: Blanket

Master (Time Frame File): 10:23:30 06-Jun-2019

Measurement	Unit	Phase	Nominal	Low Limit	Actual	High Limit	
Gamma Ray Calibration Gain		Master	1.000	0.580	1.100	1.250	

Company:	Equinor
Well:	31/5-7
Field:	7

Field: Eos
Rig Name: West Hercules
Country: Norway



Schlumberger

VISION Resistivity
Dual Frequency
Recorded Mode, Run 9
